

SDLC Approach

Selected Approach: Agile

Agile is a software development approach where the system is built step by step in small parts called iterations. Instead of building the whole system at once, the team focuses on delivering a small part of the system, then improving it based on feedback.


In each iteration, the team designs, develops, and reviews a specific feature. After that, feedback is collected from the client to make improvements in the next step. This makes the system more flexible and easier to adjust if requirements change.


Why Agile is suitable for this project


- The requirements of the system may not be fully clear at the beginning, especially when dealing with real gym management needs. Agile allows us to update and modify the system easily.
- The system can be developed gradually. For example, we can start with basic features such as member registration and membership tracking, then add more advanced features like scheduling sessions and managing payments.
- Agile encourages continuous communication with the client, which helps us get regular feedback and ensure that the system meets the actual needs of the gym.


		Name	Duration	Start	Finish	Predecessors	Resource Names	15 Mar 2026				
								F	S	S	M	T
1	 	Planning	2 days?	3/23/26, 8:00AM	3/24/26, 5:00PM		Project Manager					
2		Project idea definition	1 day?	3/23/26, 8:00AM	3/23/26, 5:00PM		Planning Coordinator					
3		Project scope definition	1 day?	3/24/26, 8:00AM	3/24/26, 5:00PM	2	Requirements Specialist					
4	 	Requirement Analysis	6 days?	3/25/26, 8:00AM	4/1/26, 5:00PM		Business Analyst					
5		Identify system requirements	2 days?	3/25/26, 8:00AM	3/26/26, 5:00PM		Requirements Analyst					
6		Gather functional requirem...	2 days	3/27/26, 8:00AM	3/30/26, 5:00PM	5	Functional Analyst					
7		Validate requirements with ...	2 days?	3/31/26, 8:00AM	4/1/26, 5:00PM	6	Client Liaison					
8	 	System Design	6 days	3/31/26, 8:00AM	4/7/26, 5:00PM		System Designer					
9		Database design	2 days	3/31/26, 8:00AM	4/1/26, 5:00PM		Database Architect					
10		System architecture design	2 days	4/2/26, 8:00AM	4/3/26, 5:00PM	9	Solution Architect					
11		User interface design	2 days	4/6/26, 8:00AM	4/7/26, 5:00PM	10	UI/UX Designer					
12	 	Implementation	9 days	4/6/26, 8:00AM	4/16/26, 5:00PM		Developer					
13		Backend development	3 days	4/6/26, 8:00AM	4/8/26, 5:00PM		Backend Developer					
14		Frontend development	3 days	4/9/26, 8:00AM	4/13/26, 5:00PM	13	Frontend Developer					
15		System integration	3 days	4/14/26, 8:00AM	4/16/26, 5:00PM	14	Integration Engineer					
16	 	Testing	4 days	4/15/26, 8:00AM	4/20/26, 5:00PM		Tester					
17		System testing	2 days	4/15/26, 8:00AM	4/16/26, 5:00PM		QA Analyst					
18		Bug fixing	2 days	4/17/26, 8:00AM	4/20/26, 5:00PM	17	QA Engineer					
19	 	Documentation & Delivery	2 days?	4/20/26, 8:00AM	4/21/26, 5:00PM		Documentation Specialist					
20		System documentation	1 day?	4/20/26, 8:00AM	4/20/26, 5:00PM		Technical Writer					
21		Final system delivery	1 day?	4/21/26, 8:00AM	4/21/26, 5:00PM	20	Deployment Coordinator					



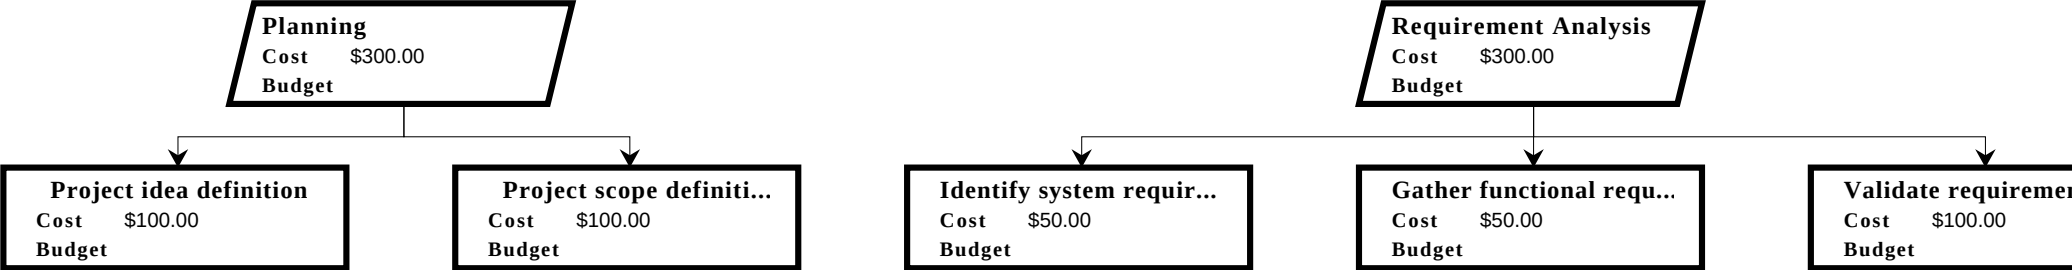

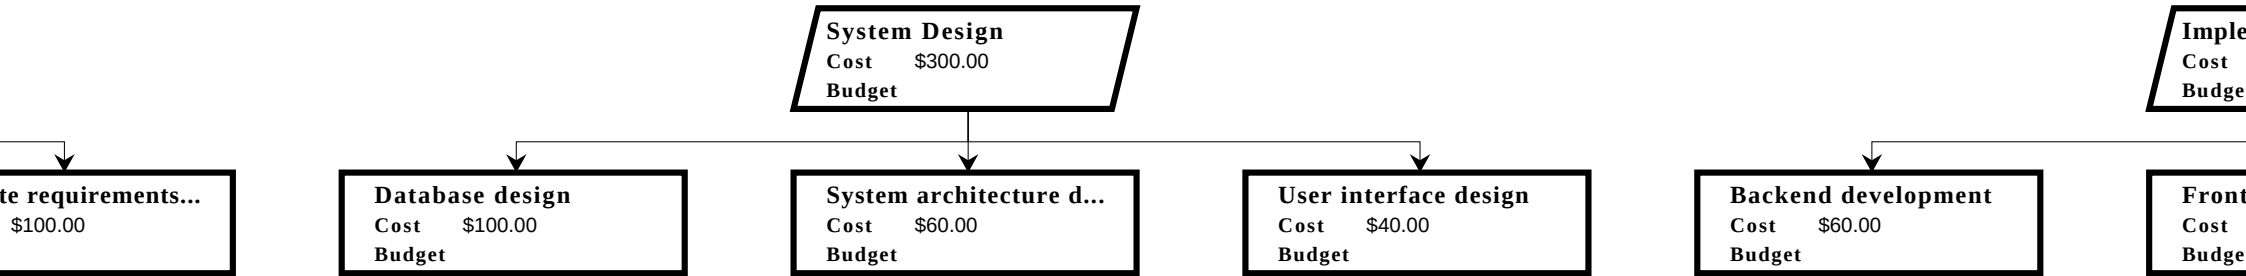

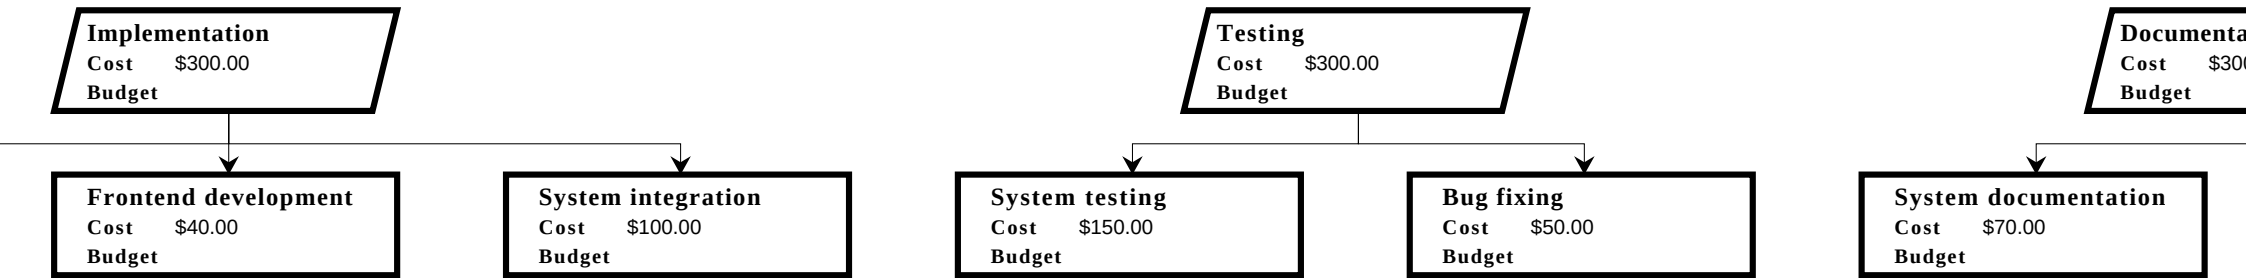

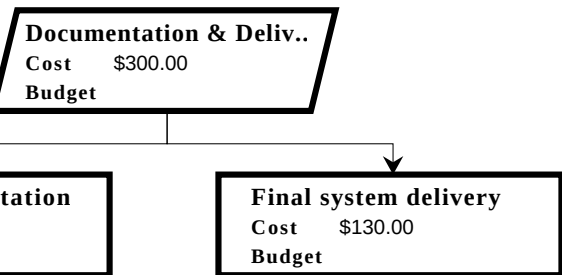

Project Manager	
Cost	\$100.00
Budget	\$0.00

Business Analyst	
Cost	\$100.00
Budget	\$0.00

System Designer	
Cost	\$100.00
Budget	\$0.00

Developer	
Cost	\$100.00
Budget	\$0.00

Tester	
Cost	\$100.00
Budget	\$0.00

\$100.00
\$0.00

Documentation Speciali...	
Cost	\$100.00
Budget	\$0.00

Planning Coordinator	
Cost	\$100.00
Budget	\$0.00

Requirements Speciali...	
Cost	\$100.00
Budget	\$0.00

Requirements Analyst	
Cost	\$50.00
Budget	\$0.00

Functional Analyst	
Cost	\$50.00
Budget	\$0.00

Functional Analyst	
Cost	\$50.00
Budget	\$0.00

Client Liaison	
Cost	\$100.00
Budget	\$0.00

Database Architect	
Cost	\$100.00
Budget	\$0.00

Solution Architect	
Cost	\$60.00
Budget	\$0.00

UI/UX Designer	
Cost	\$40.00
Budget	\$0.00

--

Backend Developer	
Cost	\$60.00
Budget	\$0.00

Frontend Developer	
Cost	\$40.00
Budget	\$0.00

Integration Engineer	
Cost	\$100.00
Budget	\$0.00

QA Analyst	
Cost	\$150.00
Budget	\$0.00

QA Engineer	
Cost	\$50.00
Budget	\$0.00

Engineer	
Cost	\$50.00
Budget	\$0.00

Technical Writer	
Cost	\$70.00
Budget	\$0.00

Deployment Coordinator	
Cost	\$130.00
Budget	\$0.00

		Name	RBS	Type	E-mail Address	Material Label
1		Project Manager		Work		
2		Business Analyst		Work		
3		System Designer		Work		
4		Developer		Work		
5		Tester		Work		
6		Documentation Specialist		Work		
7		Planning Coordinator		Work		
8		Requirements Specialist		Work		
9		Requirements Analyst		Work		
10		Functional Analyst		Work		
11		Client Liaison		Work		
12		Database Architect		Work		
13		Solution Architect		Work		
14		UI/UX Designer		Work		
15		Backend Developer		Work		
16		Frontend Developer		Work		
17		Integration Engineer		Work		
18		QA Analyst		Work		
19		QA Engineer		Work		
20		Technical Writer		Work		
21		Deployment Coordinator		Work		

Accrue At	Base Calendar
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
gym managment project - page3	

	Name	Work	Work Contour	Assignment ...		12 Mar 26							29 Mar 26							5 Apr 26						
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	
1	Project Manager	8 hours			Work		0h	8h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Planning	8 hours Flat		0 days	Work			8h																		
2	Business Analyst	48 hours			Work		0h	0h	0h	8h	8h	8h	0h	0h	8h	8h	8h	0h	0h	0h	0h	0h	0h	0h	0h	
	Requirement Analysis	48 hours Flat		0 days	Work					8h	8h	8h	0h	0h	8h	8h	8h	0h	0h	0h	0h	0h	0h	0h	0h	
3	System Designer	8 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	8h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	System Design	8 hours Flat		0 days	Work										8h											
4	Developer	8 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	8h	0h	0h	0h	
	Implementation	8 hours Flat		0 days	Work																8h					
5	Tester	8 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Testing	8 hours Flat		0 days	Work																					
6	Documentation Specialist	8 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Documentation & Delivery	8 hours Flat		0 days	Work																					
7	Planning Coordinator	8 hours			Work		0h	8h	0h	8 hours	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Project idea definition	8 hours Flat		0 days	Work			8h																		
8	Requirements Specialist	8 hours			Work		0h	0h	8h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Project scope definition	8 hours Flat		0 days	Work				8h																	
9	Requirements Analyst	16 hours			Work		0h	0h	0h	8h	8h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Identify system requirements	16 hours Flat		0 days	Work					8h	8h															
10	Functional Analyst	16 hours			Work		0h	0h	0h	8 hours	0h	0h	8h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Gather functional requirements	16 hours Flat		0 days	Work						8h	0h	0h	8h												
11	Client Liaison	16 hours			Work		0h	0h	0h	16 hours	0h	0h	0h	0h	0h	8h	8h	0h	0h	0h	0h	0h	0h	0h	0h	
	Validate requirements with client	16 hours Flat		0 days	Work										8h	8h										
12	Database Architect	16 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	8h	8h	0h	0h	0h	0h	0h	0h	0h	0h	0h	
	Database design	16 hours Flat		0 days	Work										8h	8h										
13	Solution Architect	16 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	0h	0h	8h	8h	0h	0h	0h	0h	0h	0h	0h	
	System architecture design	16 hours Flat		0 days	Work												8h	8h								
14	UI/UX Designer	16 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	8h	8h	0h	0h	0h	
	User interface design	16 hours Flat		0 days	Work																8h	8h				
15	Backend Developer	24 hours			Work		0h	0h	0h	24 hours	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	8h	8h	8h	0h	0h	
	Backend development	24 hours Flat		0 days	Work																	8h	8h	8h		
16	Frontend Developer	24 hours			Work		0h	0h	0h	8 hours	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	0h	8h	0h	
	Frontend development	24 hours Flat		0 days	Work																			8h		

[illegible]

[illegible]

	Name	Work	Duration	Start		15 Apr 26							12 Apr 26							19 Apr 26						
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	
	Functional Analysis,	16 hours	2 days	3/27/26, 8:00 AM	Work																					
7	Validate requirements with	16 hours	2 days?	3/31/26, 8:00 AM	Work																					
	Client Liaison	16 hours	2 days	3/31/26, 8:00 AM	Work																					
	Business Analysis	48 hours	6 days	3/25/26, 8:00 AM	Work																					
8	System Design	56 hours	6 days	3/31/26, 8:00 AM	Work	0h		8h	8h																	
9	Database design	16 hours	2 days	3/31/26, 8:00 AM	Work																					
	Database Architect	16 hours	2 days	3/31/26, 8:00 AM	Work																					
10	System architecture design	16 hours	2 days	4/2/26, 8:00 AM	Work																					
	Solution Architect	16 hours	2 days	4/2/26, 8:00 AM	Work																					
11	User interface design	16 hours	2 days	4/6/26, 8:00 AM	Work			8h	8h																	
	UI/UX Designer	16 hours	2 days	4/6/26, 8:00 AM	Work			8h	8h																	
	System Designer	8 hours	1 day	3/31/26, 8:00 AM	Work																					
12	Implementation	80 hours	9 days	4/6/26, 8:00 AM	Work			16h	8h	8h	8h	8h	0h	0h	8h	8h	8h	8h								
13	Backend development	24 hours	3 days	4/6/26, 8:00 AM	Work			8h	8h	8h																
	Backend Developer	24 hours	3 days	4/6/26, 8:00 AM	Work			8h	8h	8h																
14	Frontend development	24 hours	3 days	4/9/26, 8:00 AM	Work						8h	8h	0h	0h	8h											
	Frontend Developer	24 hours	3 days	4/9/26, 8:00 AM	Work						8h	8h	0h	0h	8h											
15	System integration	24 hours	3 days	4/14/26, 8:00 AM	Work											8h	8h	8h								
	Integration Engineer	24 hours	3 days	4/14/26, 8:00 AM	Work											8h	8h	8h								
	Developer	8 hours	1 day	4/6/26, 8:00 AM	Work			8h																		
16	Testing	40 hours	4 days	4/15/26, 8:00 AM	Work											16h	8h	8h	0h	0h	8h					
17	System testing	16 hours	2 days	4/15/26, 8:00 AM	Work											8h	8h									
	QA Analyst	16 hours	2 days	4/15/26, 8:00 AM	Work											8h	8h									
18	Bug fixing	16 hours	2 days	4/17/26, 8:00 AM	Work													8h	0h	0h	8h					
	QA Engineer	16 hours	2 days	4/17/26, 8:00 AM	Work													8h	0h	0h	8h					
	Tester	8 hours	1 day	4/15/26, 8:00 AM	Work											8h										
19	Documentation & Delivery	24 hours	2 days?	4/20/26, 8:00 AM	Work																16h	8h				
20	System documentation	8 hours	1 day?	4/20/26, 8:00 AM	Work																8h					
	Technical Writer	8 hours	1 day	4/20/26, 8:00 AM	Work																8h					
21	Final system delivery	8 hours	1 day?	4/21/26, 8:00 AM	Work																	8h				
	Deployment Coordinator	8 hours	1 day	4/21/26, 8:00 AM	Work																	8h				
	Documentation Specialist	8 hours	1 day	4/20/26, 8:00 AM	Work																8h					

Requirement Gathering and Client Interaction

Dealing with the client is an important part of developing the Gym Management System. The client in this project is the gym management team, so it is necessary to communicate with them clearly to understand their needs.

Dealing with the Client

- Schedule regular meetings to discuss the system and project progress
- Use simple and clear language to avoid confusion
- Listen carefully to their requirements and suggestions
- Show them progress regularly to build trust

Gathering Requirements

- Interviews: Talking directly with the gym manager and staff to understand how they manage members, subscriptions, and payments
- Observation: Watching how the current system works to identify problems
- Questionnaires: Collecting feedback from staff or members about needed features
- Document Review: Analyzing existing forms, records, or spreadsheets used in the gym

Getting Suitable Feedback

- Show simple prototypes like login pages or forms
- Ask the client to review and confirm requirements
- Collect feedback after each stage of development
- Update the system based on the feedback
